



Fredericksburg Soccer Fields  
Update for May 7, 2024



# Public/private partnership

- City of Fredericksburg
- Adams R. Scripps Foundation
- Create Healthy Foundation
- Several Local Families
- FBG Parks Foundation



# Completed Tasks

- Agreement with the city
- Site plan approved
- Construction started March 1





# In Progress

- **Light Poles Complete**
- **Irrigation Rough In 95% Complete**
- **Parking Lot Base Underway**
- **Backstop Poles In**

YSO UNITED

# Construction Team

- City of Fredericksburg-Water, Sewer, Electric Service
- Allen Keller Company-Dirt Work
- Texas Multi-Chem- Irrigation and Turf
- DW Electric-Lights
- DR Welding-Maintenance Shed
- Farm and Home Improvements-Fence
- Mustard Design
- Mabery Construction-Restrooms





# Next Steps

- Finish field utilities
- Topsoil
- Plant grass June 1
- Maintenance shed
  - Acquire field equipment
- Parking Lot
- Kickoff in September!
- Restrooms






# Extras

- **Fredericksburg Parks Foundation will provide trees.**
- **Trail system can be built in future around the site.**



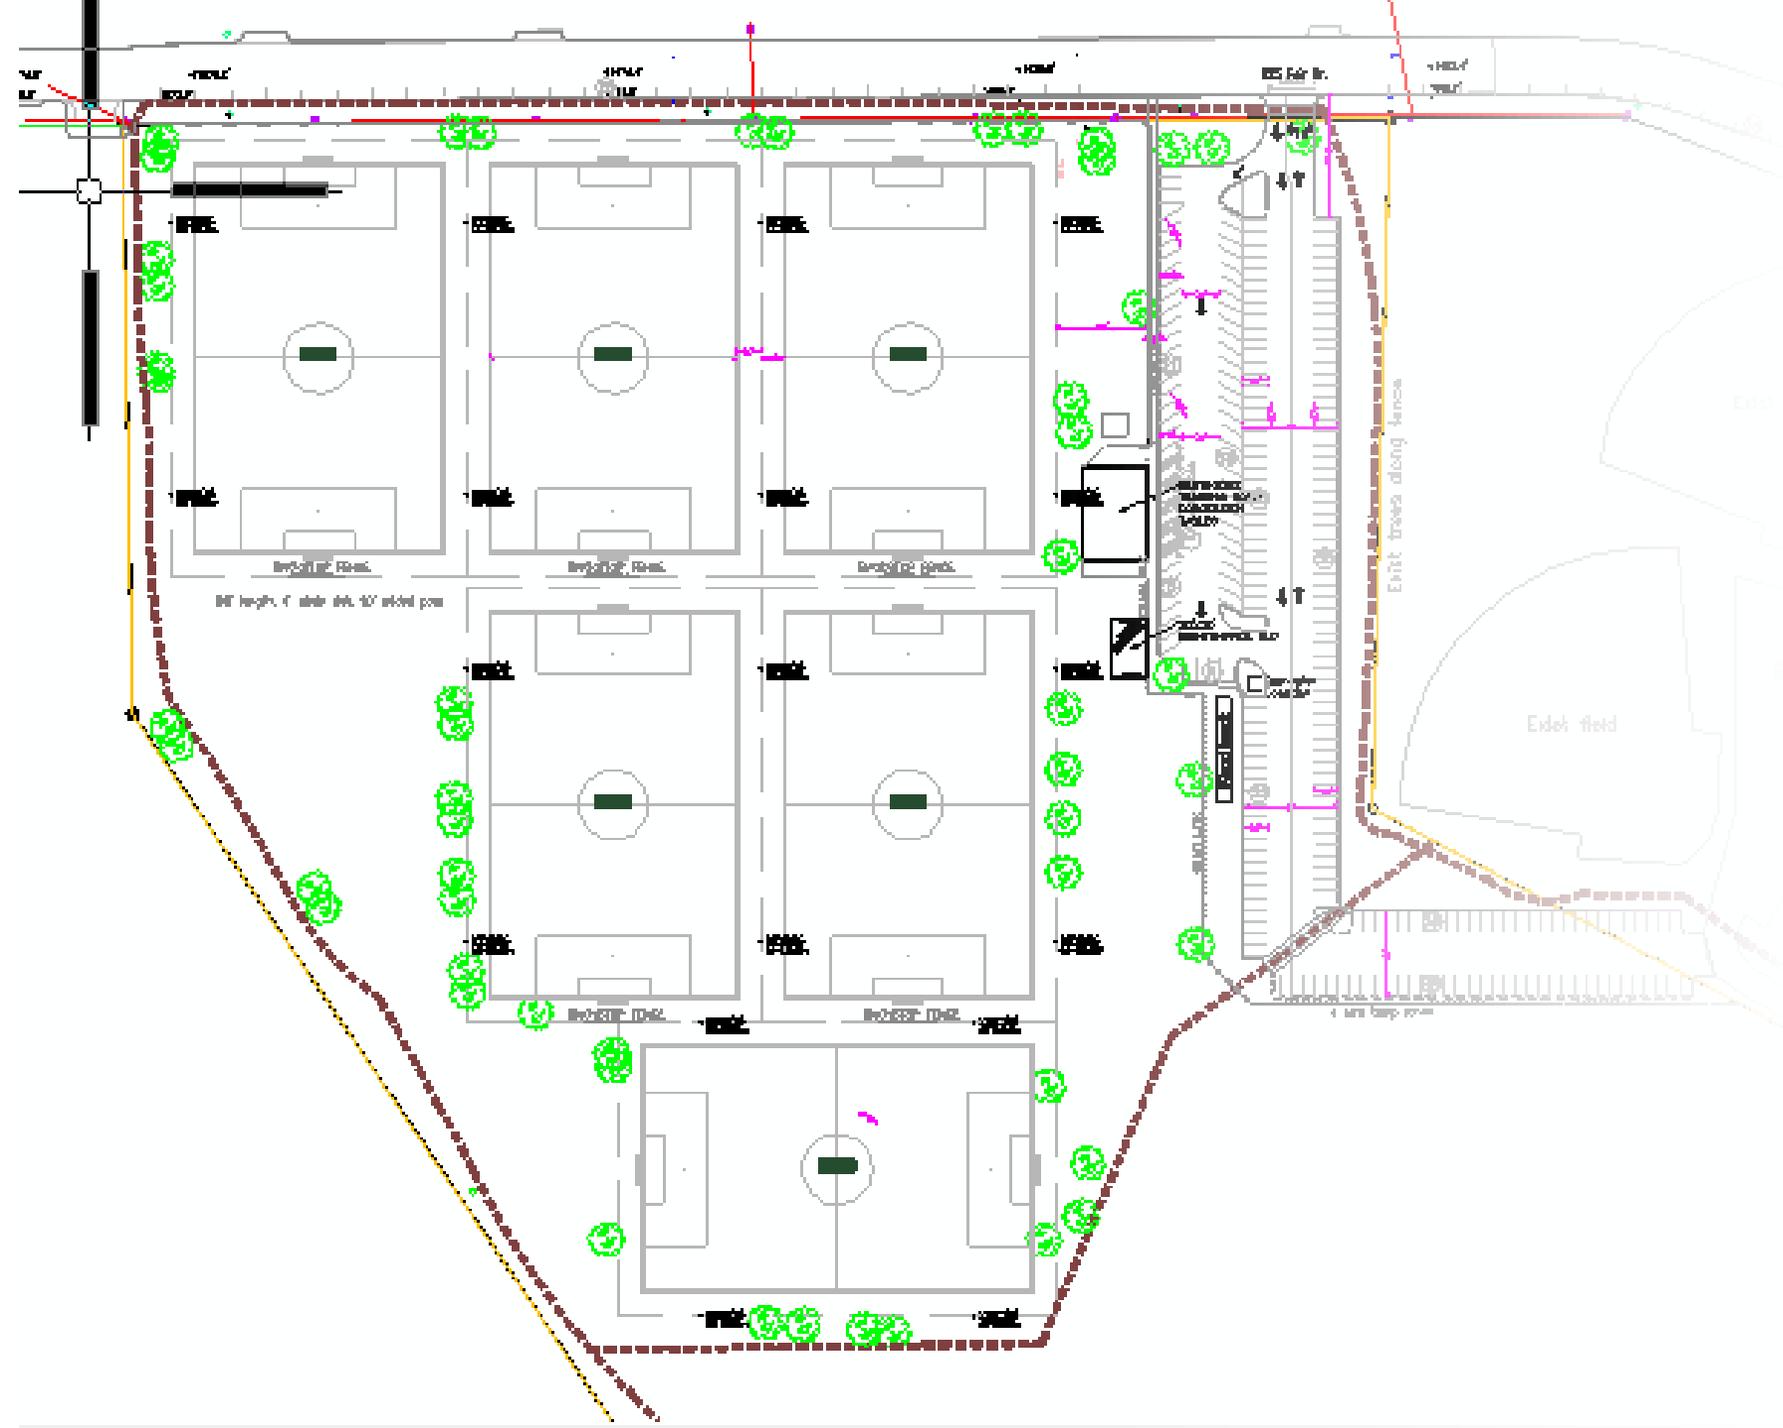

# Tree and Trail Plan

